



363 Centennial Parkway, Suite 210
Louisville, CO 80027
Telephone (303) 665-4390
Facsimile (303) 665-4391

September 11, 2007

Via U.S. Mail

Mr. Scott Miller
U.S. Environmental Protection Agency, Region IV
4WD-SRTMB
61 Forsyth Street, S.W.
Atlanta, Georgia 30303-3104

Subject: August 2007 Monthly Progress Report

Dear Mr. Miller:

On behalf of Beazer East, Inc. (Beazer), attached is the August 2007 Monthly Progress Report for the Cabot Carbon/Koppers Superfund Site in Gainesville, Florida as required by 1991 Unilateral Administrative Order (UAO) and the 1994 UAO Amendment. If you have any questions or comments, please contact me at (303) 665-4390.

Sincerely,

A handwritten signature in black ink that reads "Gaius Roemer".

Gaius Roemer, P.E.
Senior Engineer

Enclosure

cc: J. Mousa (ACEPD)
K. Helton (FDEP)
M. Slenska (BEI)
M. Brouman (BEI)
P. Salisbury (KI)
J. Fankulewski (KI)

August 2007
MONTHLY PROGRESS REPORT
Cabot Carbon/Koppers Superfund Site
GAINESVILLE, FLORIDA

1. DESCRIPTION OF ACTIONS TAKEN TO COMPLY WITH THE UNILATERAL ADMINISTRATIVE ORDER (MARCH 1991) AND ESTIMATE OF THE PERCENTAGE OF THE RD/RA COMPLETED:

- Beazer's Operation and Maintenance (O&M) Contractor performed routine treatment plant operation and maintenance services for the ground water remedial system.
- Second Five-Year Review Report recommendations are being performed through 2007.

2. SUMMARY OF RESULTS OF SAMPLING AND TESTS AND ALL OTHER DATA DURING THE MONTH:

- Instantaneous flow rates and totalizer volumes were measured in each extraction well.
- 9.5 gallons of NAPL were bailed from the Hawthorn Group wells during the past month, and a total of 200.01 gallons have been bailed since the start of the NAPL recovery program in June 19, 2004. The two-week recovery schedule was started October 25, 2005.
- A total of 999,000 gallons of ground water were recovered by the existing extraction system, treated and discharged to the Gainesville Regional Utilities (GRU) during this past month (operating period of 694 hours). The average recovery rate for the month was approximately 24.0 gallons per minute (gpm).

3. SUMMARY OF ALL PLANS, REPORTS, DELIVERABLES AND PROCEDURES COMPLETED:

- Completed monthly maintenance check.
- Inspected piezometers, extraction wells, piping, valves, treatment plant vessels and controls, buildings and grounds.
- Cleaned ferric chloride pump and static mixer.
- Repaired/replaced EW-3, EW-5, EW-6, EW-9, EW-11 pumps.
- Vacuumed stormwater from well houses.
- Completed sampling of recently redeveloped Surficial Aquifer monitoring wells.
- Submitted 2007 First Semiannual Groundwater Monitoring Report.
- Submitted 2007 2nd Quarter Upper Floridan Aquifer Monitoring Report.
- Began Hawthorn well installation.
- Began Hawthorn NAPL recovery pilot test activities.
- Began ISBS pilot test activities.

4. PROJECTED WORK FOR THE NEXT MONTH (SEPTEMBER 2007) WITH SCHEDULE CONSIDERATIONS:

(Please see the attached draft schedule. Note that this is a working schedule and is likely to change.)

- Measure instantaneous flow rates and totalizer volumes for each extraction well.
- Continue NAPL removal from Hawthorn Group wells on a two-week schedule.
- Continue Hawthorn monitoring well installation.
- Submit Floridan Well Installation Report (FW-24B & 4 LTZ wells).
- Perform 3rd quarter sampling event for UF wells.
- Continue Hawthorn well installation.
- Continue Hawthorn NAPL recovery pilot test activities.
- Continue ISBS pilot test activities.
- Submit Surficial NAPL recovery pilot test workplan.

5. SUMMARY OF PROBLEMS OR POTENTIAL PROBLEMS AND ACTUAL OR ANTICIPATED DELAYS ENCOUNTERED DURING THE MONTH:

- None this reporting period.

6. ACTIONS BEING TAKEN TO RECTIFY PROBLEMS OR DELAYS:

- None this reporting period.


7. SUPPLEMENTAL INFORMATION:

- Please see the attached draft schedule. Note that this is a working schedule and is likely to change.

8. CHANGES IN PERSONNEL DURING THIS MONTH:

- None this reporting period.


Cabot Carbon/Koppers Site: Combined Beazer USEPA Schedule (DRAFT FOR DISCUSSION)

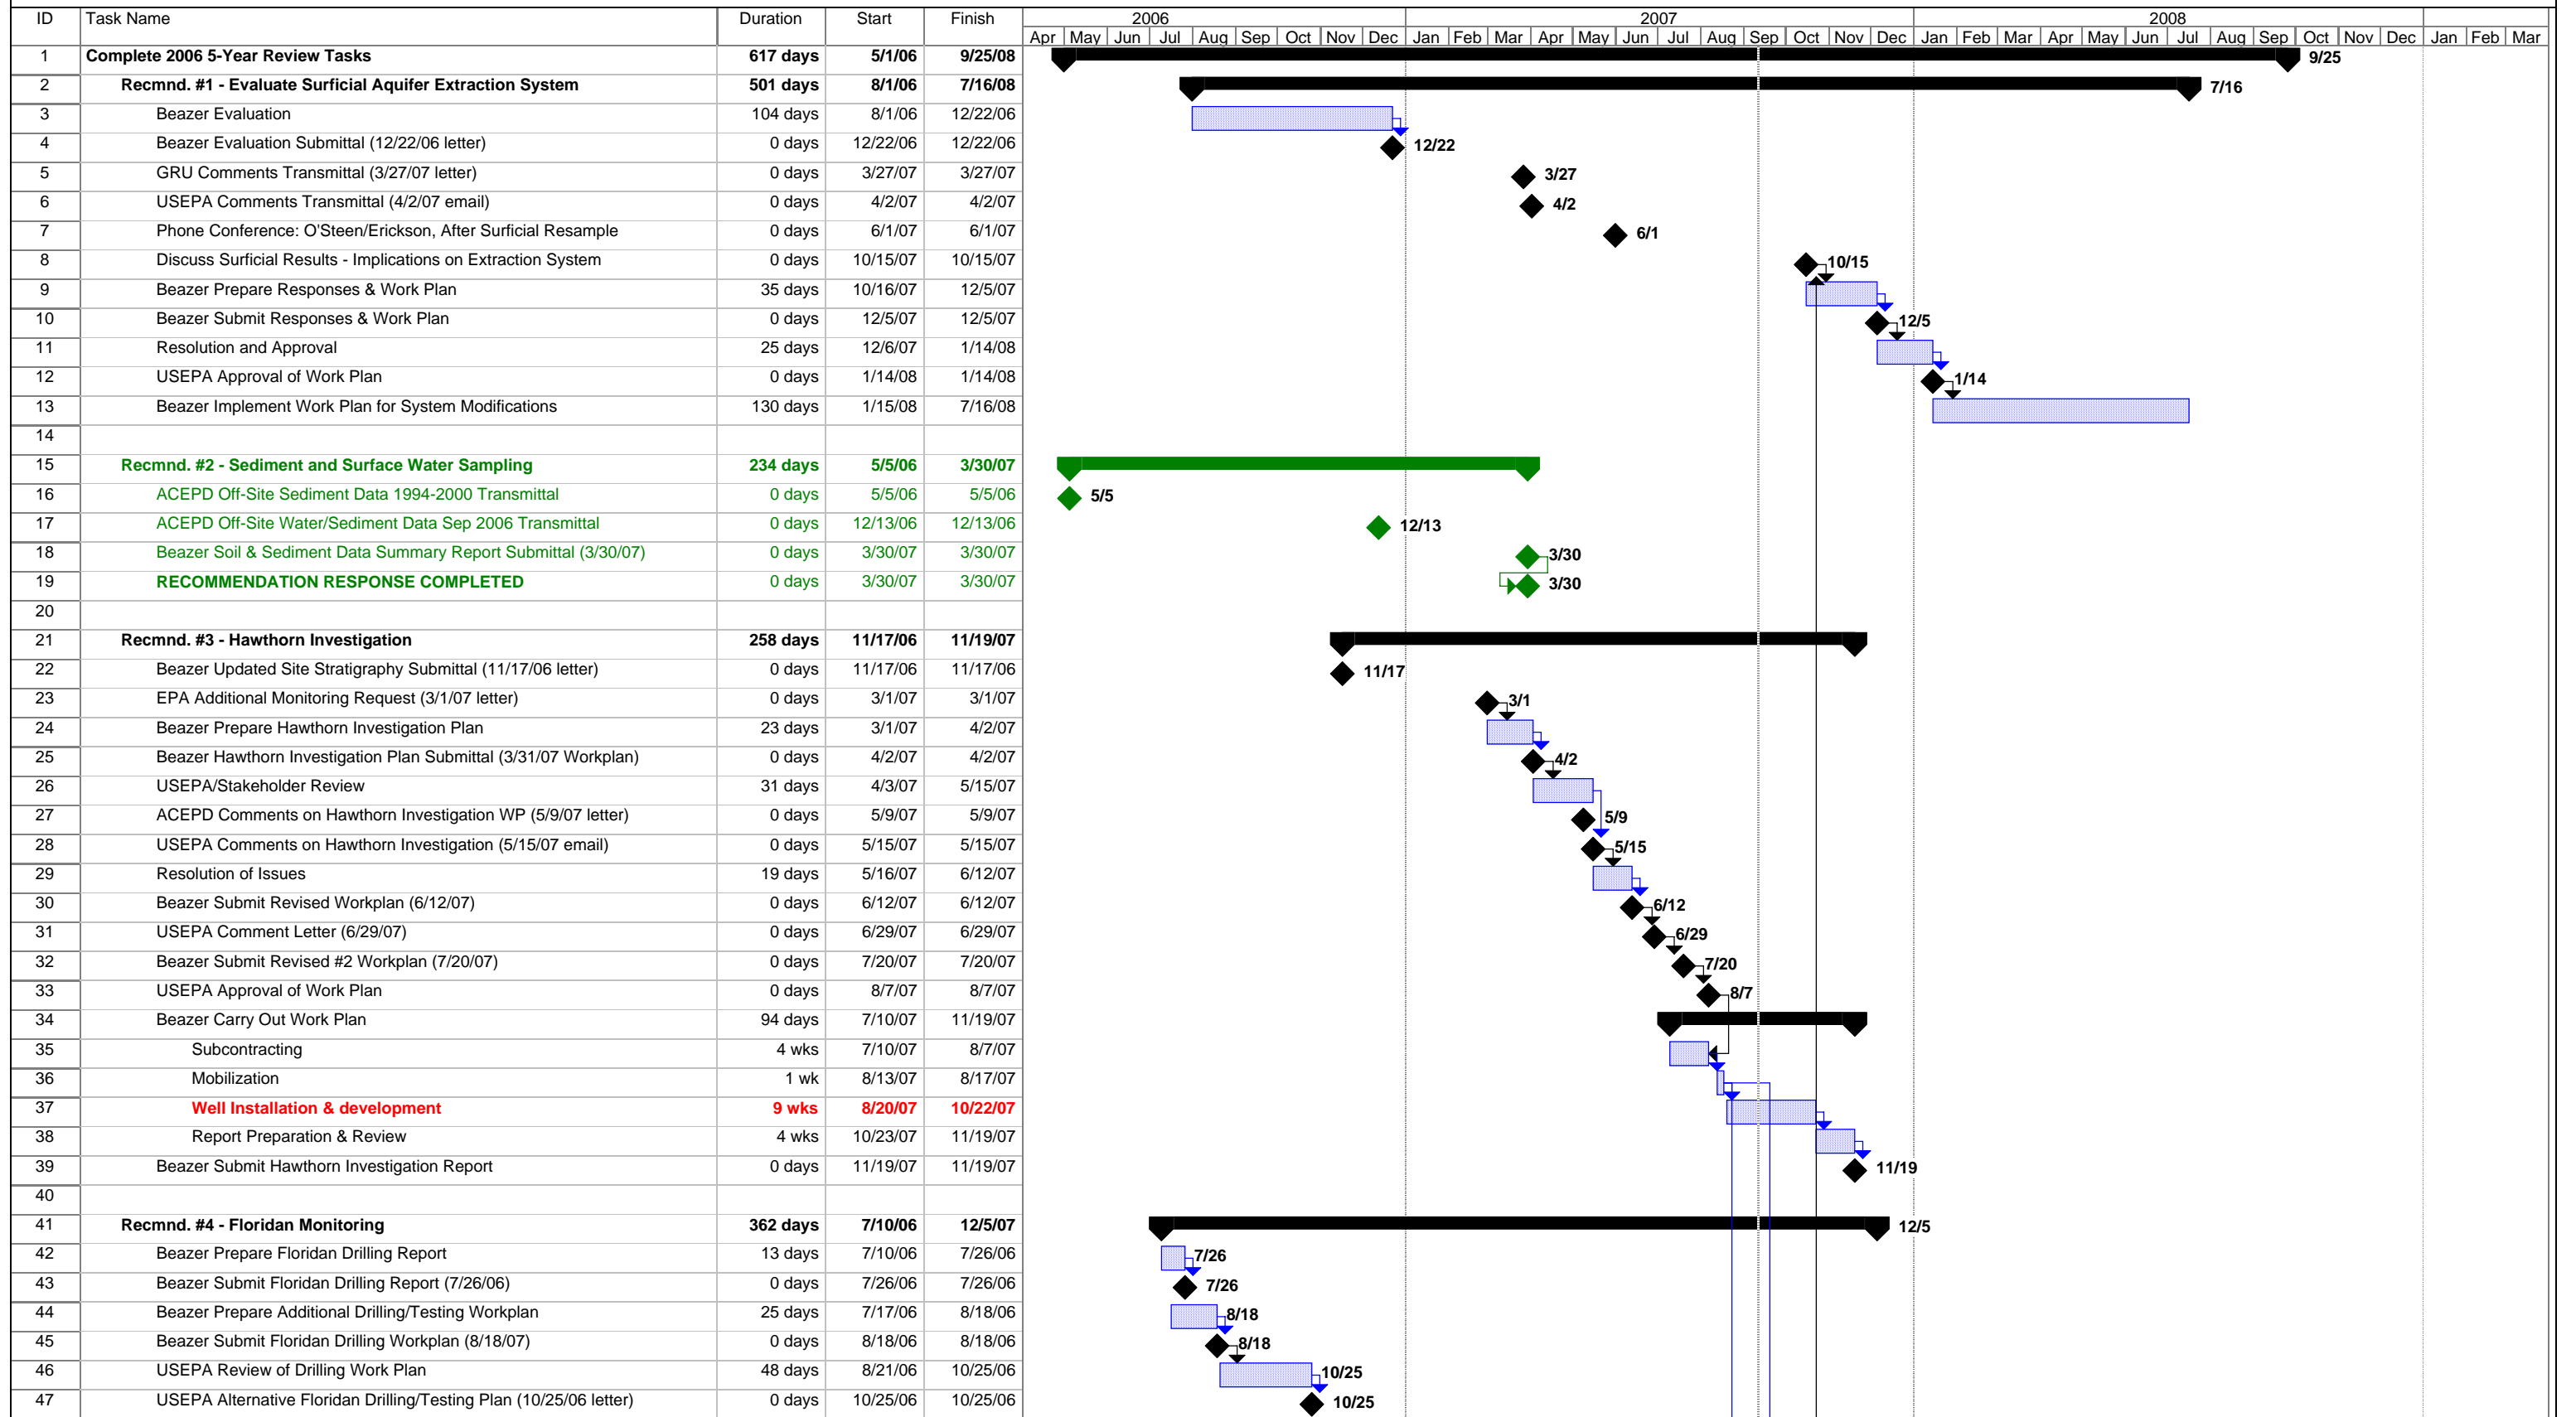

Date: 9/11/07
Current/In-Progress Item
Completed Major Task

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

Cabot Carbon/Koppers Site: Combined Beazer USEPA Schedule (DRAFT FOR DISCUSSION)

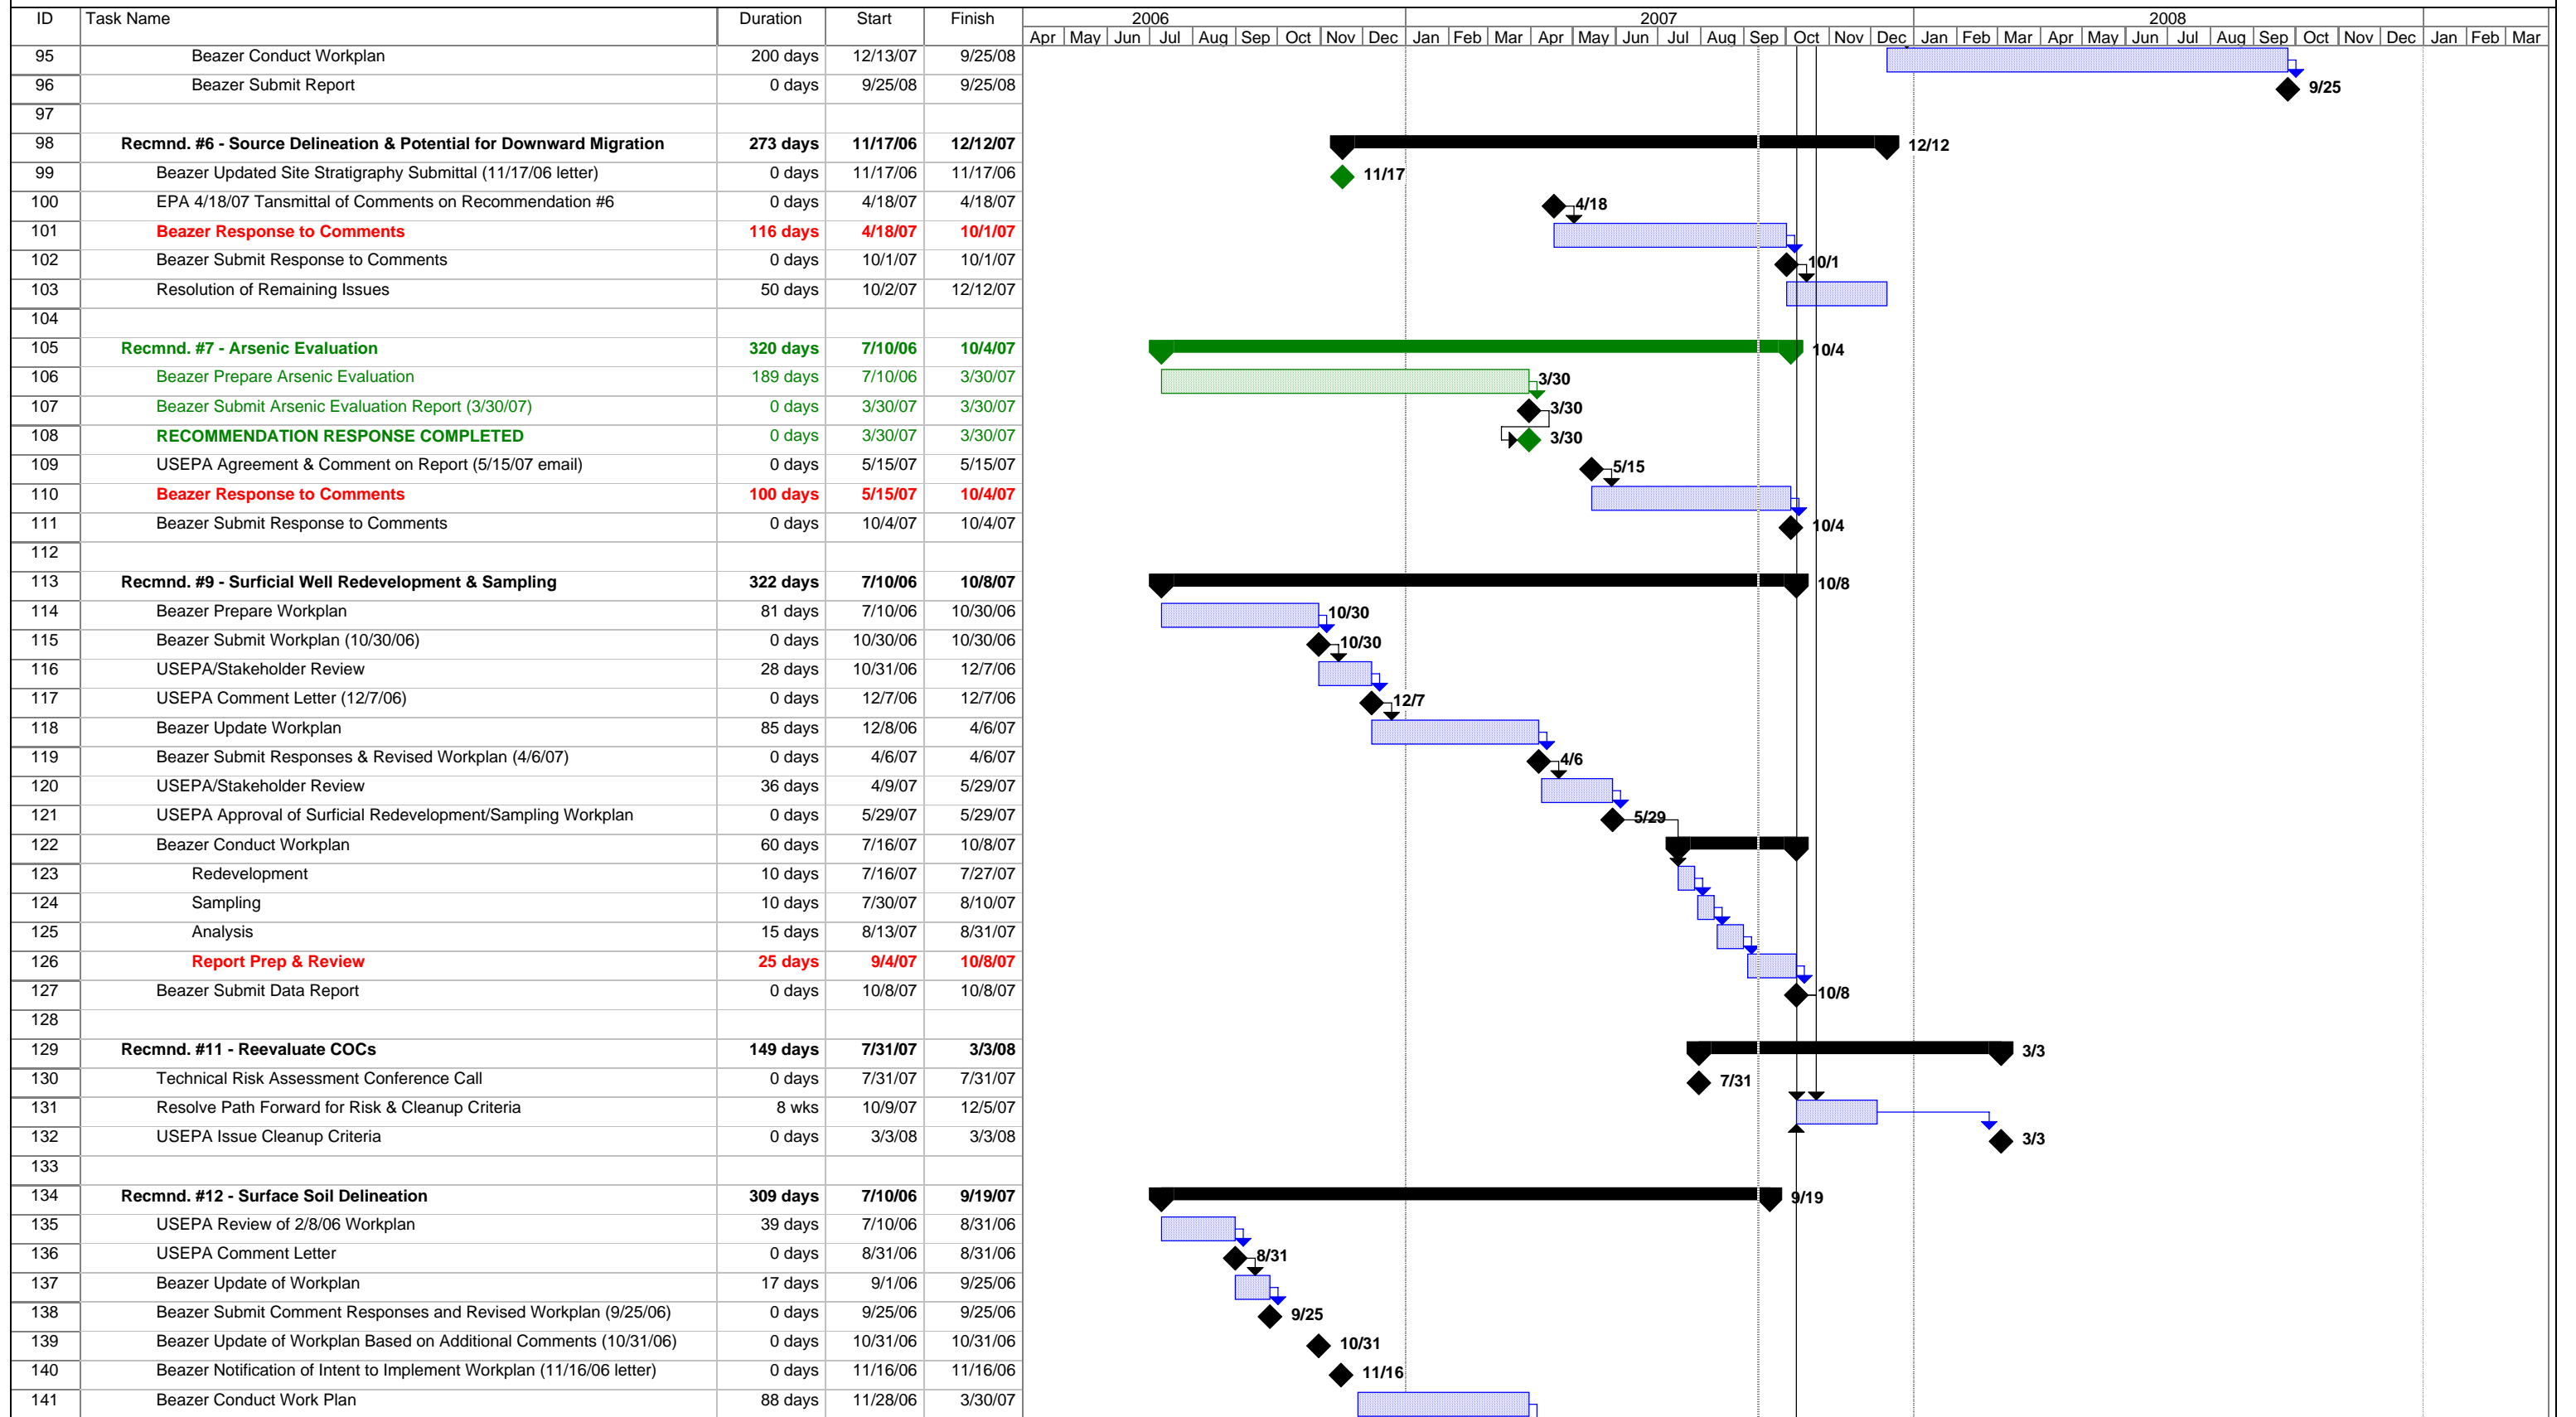

Date: 9/11/07
Current/In-Progress Item
Completed Major Task

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

