



363 Centennial Parkway, Suite 210
Louisville, CO 80027
Telephone (303) 665-4390
Facsimile (303) 665-4391

November 19, 2007

Via U.S. Mail

Mr. Scott Miller
U.S. Environmental Protection Agency, Region IV
4WD-SRTMB
61 Forsyth Street, S.W.
Atlanta, Georgia 30303-3104

Subject: October 2007 Monthly Progress Report

Dear Mr. Miller:

On behalf of Beazer East, Inc. (Beazer), attached is the October 2007 Monthly Progress Report for the Cabot Carbon/Koppers Superfund Site in Gainesville, Florida as required by 1991 Unilateral Administrative Order (UAO) and the 1994 UAO Amendment. If you have any questions or comments, please contact me at (303) 665-4390.

Sincerely,

A handwritten signature in black ink that reads "Gaius Roemer".

Gaius Roemer, P.E.
Senior Engineer

Enclosure

cc: J. Mousa (ACEPD)
K. Helton (FDEP)
M. Slenska (BEI)
M. Brouman (BEI)
P. Salisbury (KI)
J. Fankulewski (KI)

October 2007
MONTHLY PROGRESS REPORT
Cabot Carbon/Koppers Superfund Site
GAINESVILLE, FLORIDA

1. DESCRIPTION OF ACTIONS TAKEN TO COMPLY WITH THE UNILATERAL ADMINISTRATIVE ORDER (MARCH 1991) AND ESTIMATE OF THE PERCENTAGE OF THE RD/RA COMPLETED:

- Beazer's Operation and Maintenance (O&M) Contractor performed routine treatment plant operation and maintenance services for the ground water remedial system.
- Second Five-Year Review Report recommendations are being performed through 2007.

2. SUMMARY OF RESULTS OF SAMPLING AND TESTS AND ALL OTHER DATA DURING THE MONTH:

- Instantaneous flow rates and totalizer volumes were measured in each extraction well.
- 12.3 gallons of NAPL were bailed from the Hawthorn Group wells during the past month (3 recovery events), and a total of 218.96 gallons have been bailed since the start of the NAPL recovery program in June 19, 2004. The two-week recovery schedule was started October 25, 2005.
- A total of 1,138,000 gallons of ground water were recovered by the existing extraction system, treated and discharged to the Gainesville Regional Utilities (GRU) during this past month (operating period of 757.4 hours). The average recovery rate for the month was approximately 25.0 gallons per minute (gpm).

3. SUMMARY OF ALL PLANS, REPORTS, DELIVERABLES AND PROCEDURES COMPLETED:

- Completed monthly maintenance check.
- Inspected piezometers, extraction wells, piping, valves, treatment plant vessels and controls, buildings and grounds.
- Repaired/replaced EW-10 pump.
- Vacuumed stormwater from well houses.
- Clean static mixer and ferric chloride pump.
- All offsite Hawthorn monitoring wells have been completed and developed except HG-22D.
- Submitted a revised surface soil sampling data report
- Submitted a report on the installation and testing of new Floridan Aquifer wells
- Held a working session with USEPA to identify and screen technologies for potential use in the comprehensive Site remedy

4. PROJECTED WORK FOR THE NEXT MONTH (NOVEMBER 2007) WITH SCHEDULE CONSIDERATIONS:

(Please see the attached draft schedule. Note that this is a working schedule and is likely to change.)

- Measure instantaneous flow rates and totalizer volumes for each extraction well.
- Continue NAPL removal from Hawthorn Group wells on a two-week schedule.
- Submit 3rd quarter Upper Floridan Sampling Report.
- Continue well installation activities at HG-22D.

- Continue Hawthorn NAPL recovery pilot test construction activities.
- Continue ISBS pilot test preparation activities.

5. SUMMARY OF PROBLEMS OR POTENTIAL PROBLEMS AND ACTUAL OR ANTICIPATED DELAYS ENCOUNTERED DURING THE MONTH:

- A public-utility sewer line was accidentally damaged during drilling of Hawthorn Group well HG-22D just west of the site property line. The incident has caused minor delays in the drilling program.

6. ACTIONS BEING TAKEN TO RECTIFY PROBLEMS OR DELAYS:

- Gainesville Regional Utilities (GRU) and GeoTrans have communicated frequently regarding the incident at HG-22D.


7. SUPPLEMENTAL INFORMATION:

- Please see the attached draft schedule. Note that this is a working schedule and is likely to change.

8. CHANGES IN PERSONNEL DURING THIS MONTH:

- None this reporting period.

Cabot Carbon/Koppers Site: Combined Beazer USEPA Schedule (DRAFT FOR DISCUSSION)

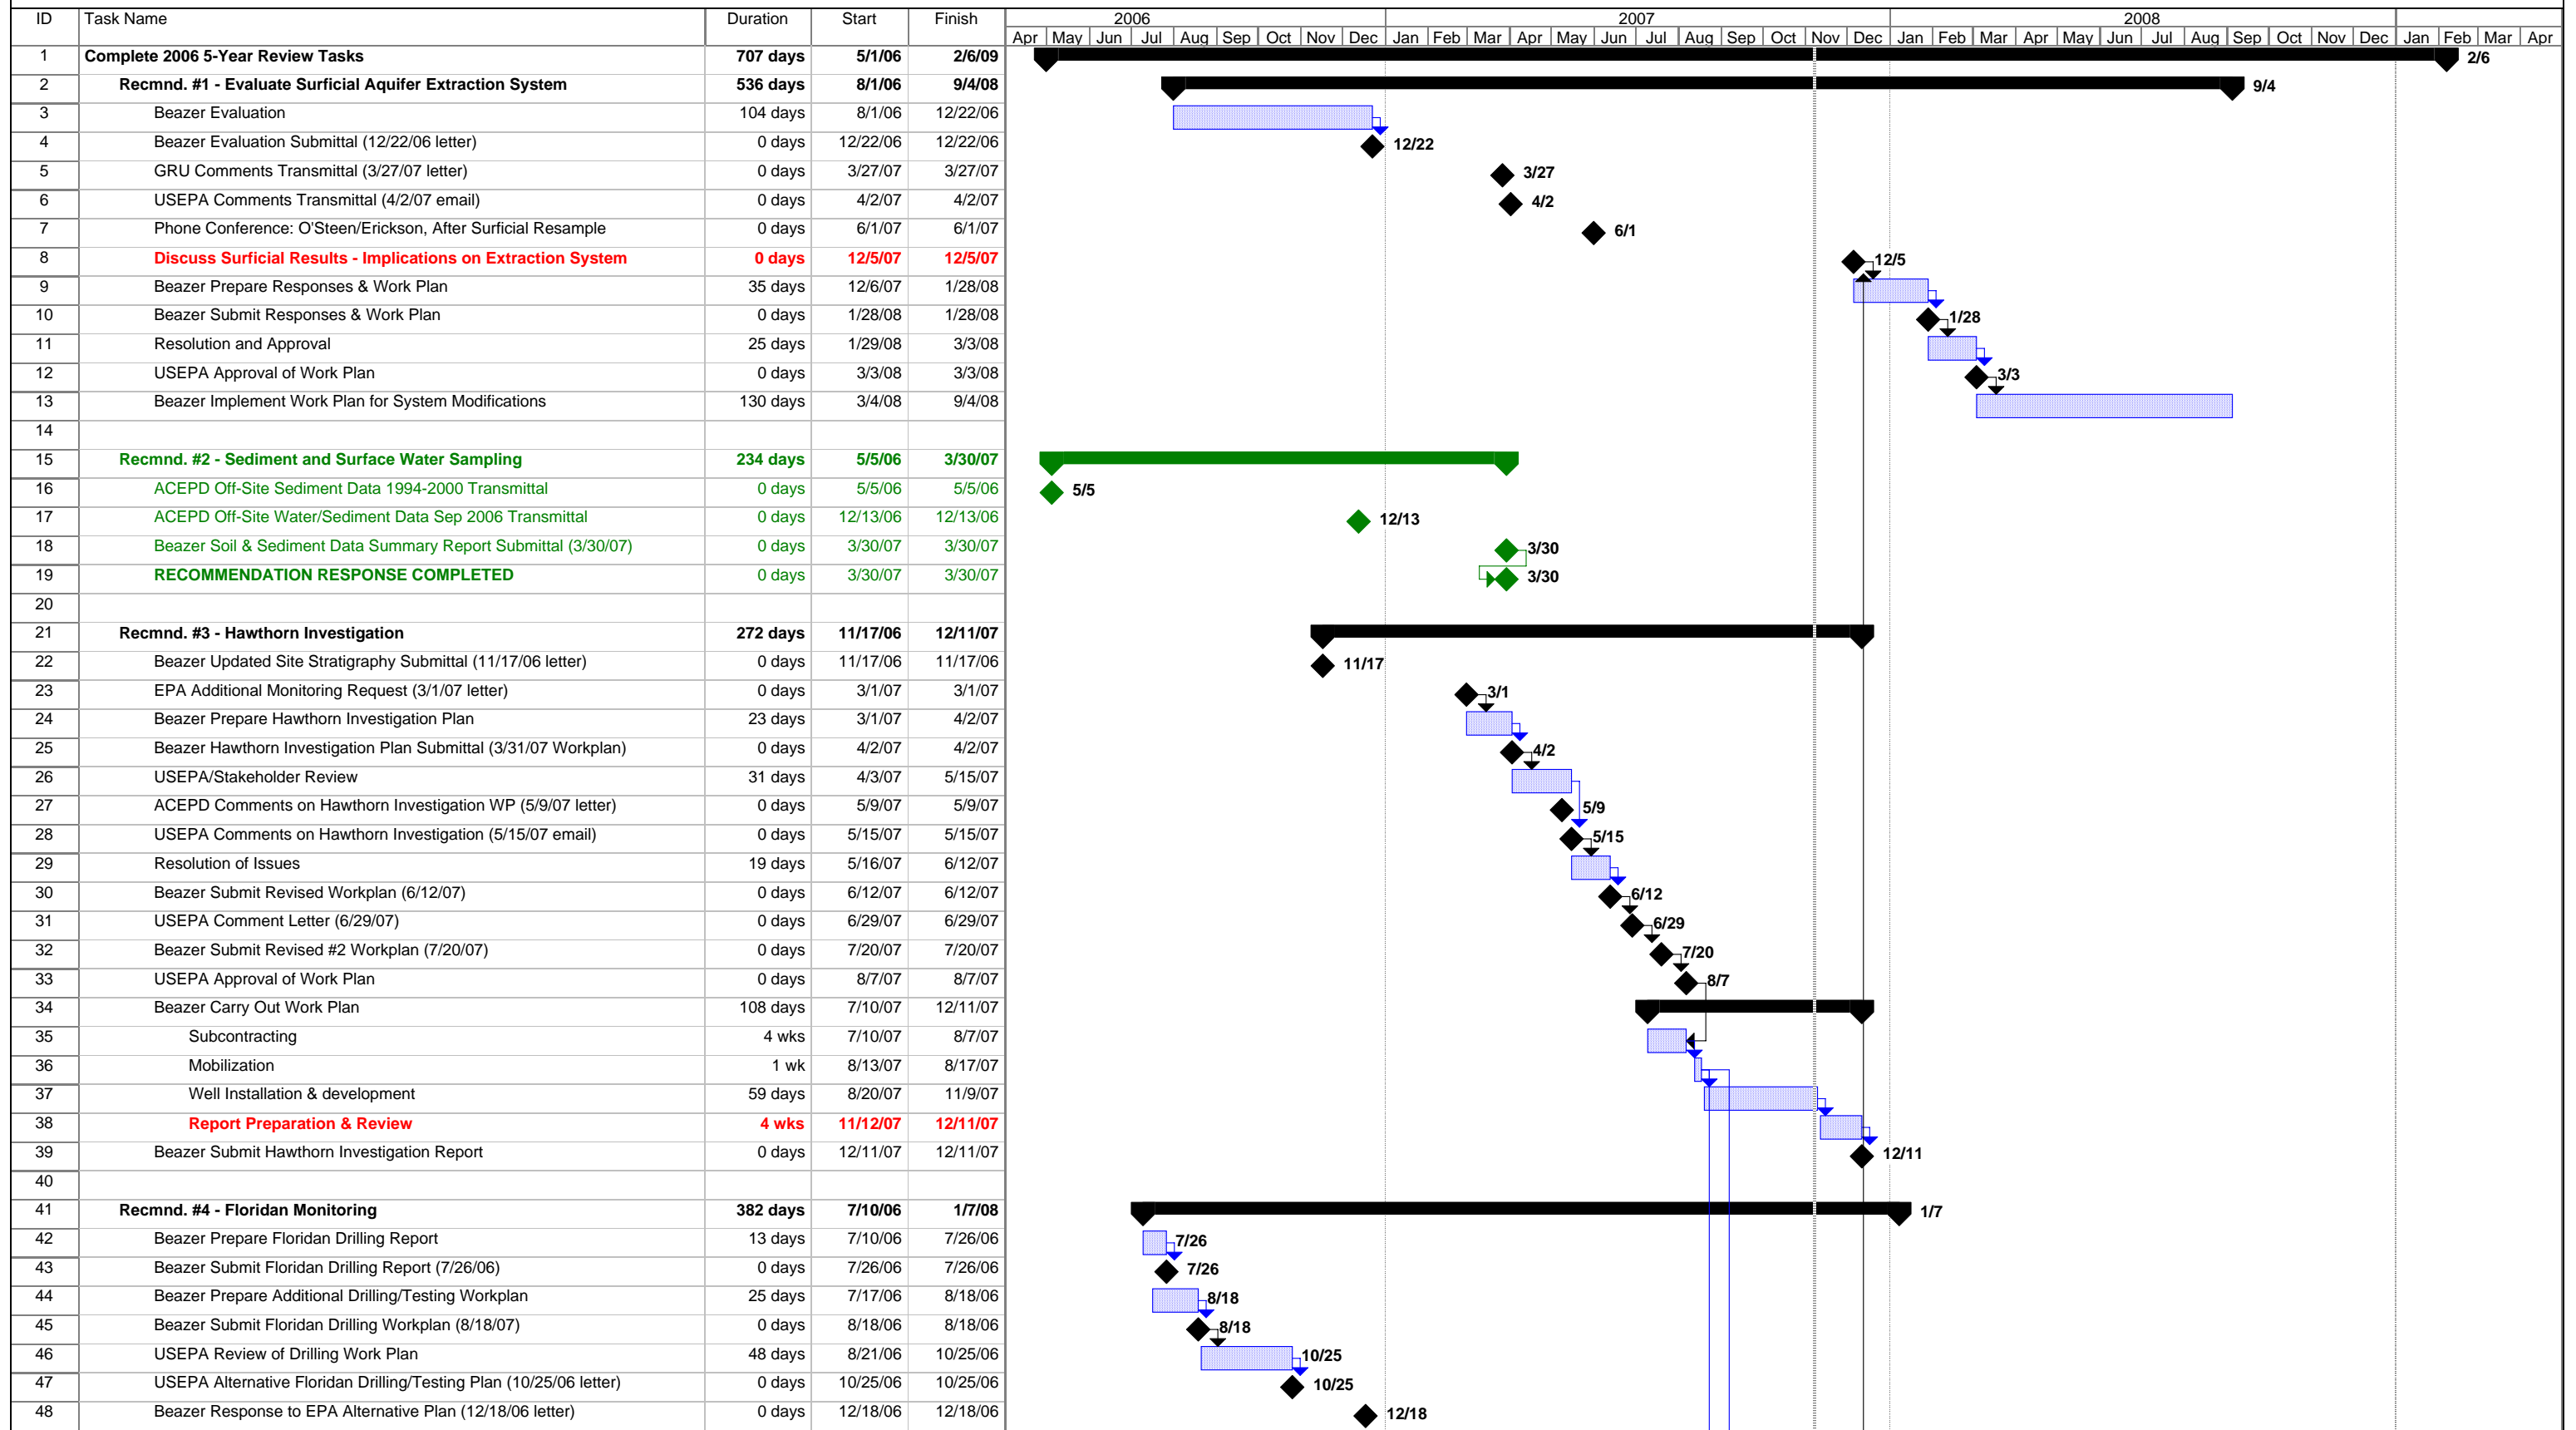

Date: 11/7/07


Current/In-Progress Item

Completed Major Task

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone

Cabot Carbon/Koppers Site: Combined Beazer USEPA Schedule (DRAFT FOR DISCUSSION)

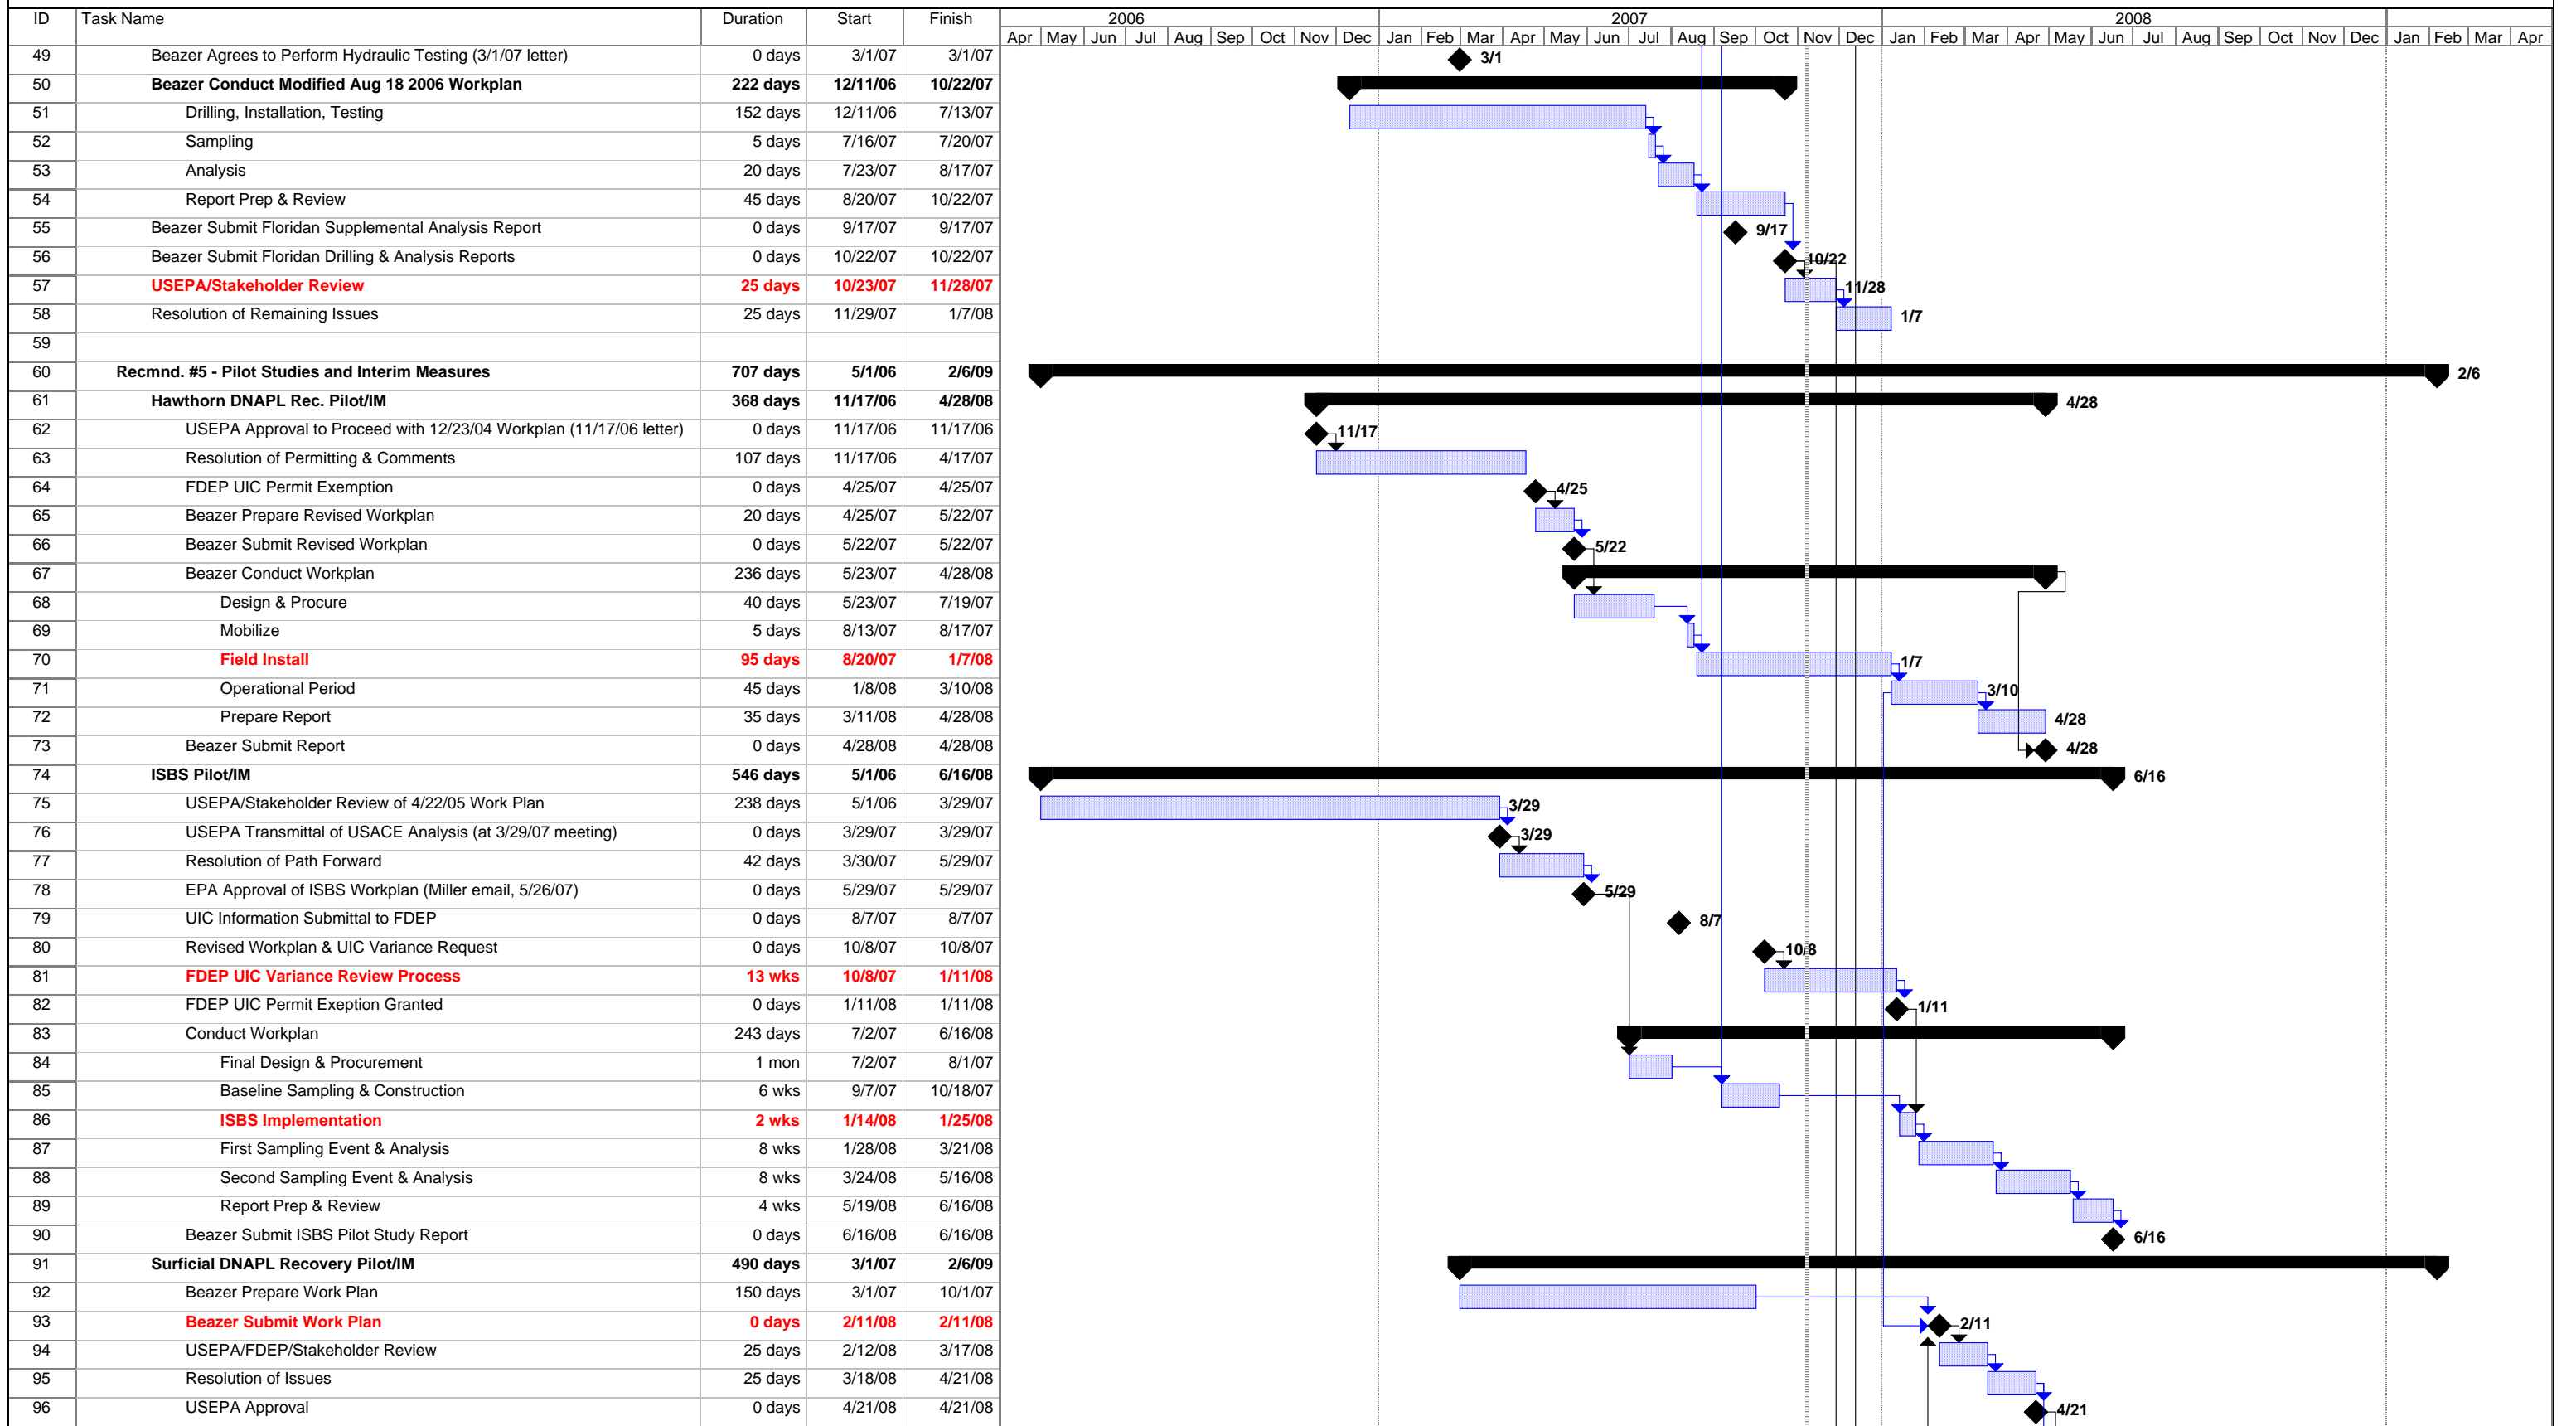

Date: 11/7/07
Current/In-Progress Item
Completed Major Task

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

